

WELCOME TO BARC DELEGATES

KICK-OFF MEETING AND BARC PROJECTS STATUS

DATE: 15.05.2026



**Manufacturing ,Testing And Supply of Stud Tension Equipment
Type-1,2,3,4,5,6,7 Along With Accessories**

Kick off meeting on 6th April 2026

1/N/072/S5/STE Dated on 17 NOV 2025

Customers: ATVP and BARC, Delivery to SBC, Vizag.

Project outlay: 24,76,70,784 + GST

Project duration: 20 Months (STE Type - 1)
26 Months (Others)

Project Coordinator: Anil Kumar K

Design: Mukkanneshwara K N ,Mohammed Arfath Hussain

Manufacturing: V R Raju, Vignesh

Assembly : Sandeepa K R

Inspection : Kushuboo, Siddaraju

Quality: Champuri Srinivas Rao

SCOPE OF SUPPLY

Item No.	Deliverables	Quantity (set)
1.	STUD TENSION EQUIPMENT TYPE-1	01
2.	STUD TENSION EQUIPMENT TYPE- 2	01
3.	STUD TENSION EQUIPMENT TYPE- 3	01
4.	SINGLE MODULE STE M120 TYPE- 4	04
5.	SINGLE MODULE STE M85 TYPE- 5	02
6.	SINGLE MODULE STE M110 TYPE- 6	02
7.	SINGLE MODULE STE M68 TYPE- 7	02



SCOPE OF SUPPLY


Accessories

8.	MOCK-UP STAND STE(TYPE-1,2 & 3)	3 Set
9	MOCK-UP STAND STE(TYPE-4,5,6 & 7)	4 Set
10.	PLATFORM FOR MOCK-UP STAND	3 Set
11	HYDRAULIC PRESSURE INTENSIFIER (WATER BASED)	3 No's
12	HYDRAULIC PRESSURE INTENSIFIER (OIL BASED)	02 No's
13	DM WATER CONNECTIONS AND FITTINGS	-
14	OIL LINE CONNECTIONS AND FITTINGS	04
15	METALLIC PRESERVATION CONTAINERS FOR STE (TYPE 1, 2, 3, 4, 5 ,6 & 7)	04
16	CROSS BEAM ASSEMBLY	01
17	VACUUM PUMP ASSEMBLY	01


SCOPE OF WORK

1. Manufacture, Inspection, Functional Testing And Supply of Following:
 - 1.1 Stud Tensioning Equipment (Type-1, 2, 3)- 1 Set for each type
 - 1.2 Single Module Stud Tensioning Equipment (Type-4) - 4 Set
 - 1.3 Single Module Stud Tensioning Equipment (Type-5, 6, 7) - 2 Set for each type
2. Mock-ups/Trials To Establish Manufacturing Process And Demonstration of Design Load Carrying Capacity.
3. Submission of Fabrication Drawings, Specifications And Manufacturing Documents For Purchaser's Approval.
4. Procurement of Raw Materials, Consumables, Ready To Use Components Etc., For Successful Accomplishment of Respective STE Function.
5. Preservation Container For Long Preservation of STEs.
6. Pre-dispatch Inspection, Preservation And Safe Delivery of


PROJECT :STUD TENSIONING EQUIPMENT TYPE - 1

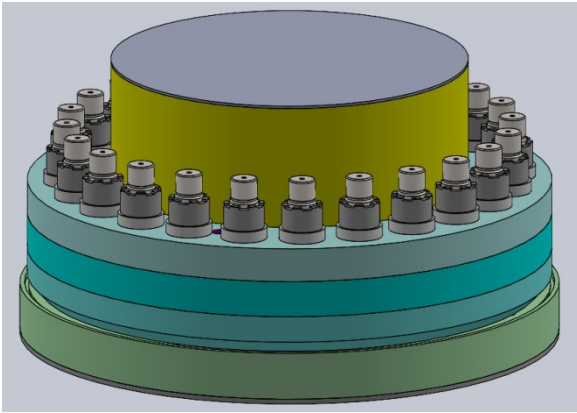


MOCKUP STAND

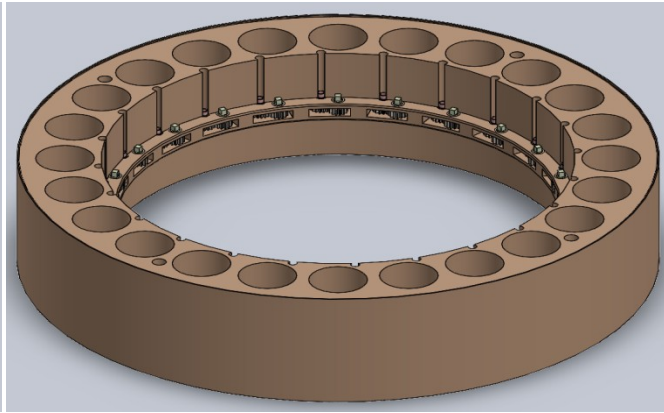

BASE RING

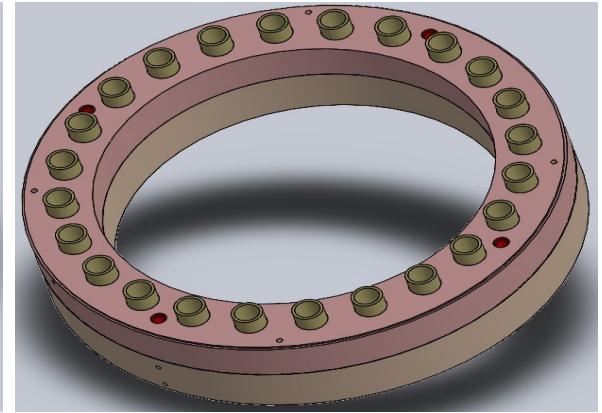

STE

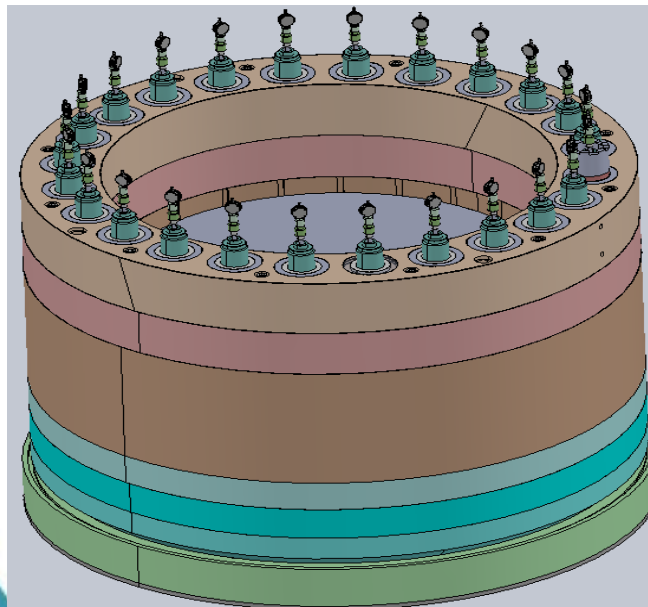

STE TYPE-1 ASSEMBLY



[illegible]

STATUS OF DOCUMENTATION:

SL.NO.	DESCRIPTION	QTY	STATUS
1.	STUD TENSION EQUIPMENT TYPE-1	01	3D & DRAWING COMPLETED
2.	STUD TENSION EQUIPMENT TYPE- 2	01	3D MODEL STARTED,NOT YET COMPLETED
3.	STUD TENSION EQUIPMENT TYPE- 3	01	3D MODEL STARTED,NOT YET COMPLETED
4.	SINGLE MODULE STE M120 TYPE- 4	04	NOT YET STARTED
5.	SINGLE MODULE STE M85 TYPE- 5	02	NOT YET STARTED
6.	SINGLE MODULE STE M110 TYPE- 6	02	NOT YET STARTED
7.	SINGLE MODULE STE M68 TYPE- 7	02	NOT YET STARTED
8.	MOCK-UP STAND STE(TYPE-1,2 & 3)	3 Set	NOT YET STARTED
9	MOCK-UP STAND STE(TYPE-4,5,6 & 7)	4 Set	NOT YET STARTED
10.	PLATFORM FOR MOCK-UP STAND	3 Set	NOT YET STARTED

Description	status
Raw material list	Completed (Manufacturing validation is currently underway)
QAP	Completed(currently undergoing secondary quality assurance review)
PERT Chart	Completed
Puller Rod Mechanical Testing(17-4-PH)	Completed
3D modeling changes in STE-1	Completed
Mockup scheme , Drawings and Material procurement	In progress execution has commenced
PVD Coating and coating process	Item submitted for surface treatment/coating phase
Equivalent material E550 BR	

TRIALS :

- **PULLER ROD IMPACT STRENGTH TRIALS ARE IN PROGRESS**
- **SS PISTON CHROME AND MOLYBDENUM COATING SPUTTERING IS IN PROGRESS**



PROJECT REVIEW MEETING


PROJECT	MANUFACTURING AND SUPPLY OF SPECIAL TOOLINGS AND EQUIPMENTS
ATVP PO NO	1/N/072/REF/EQPT, 27 TH JAN 2025
CMTI PROJECT NO AND VALUE	GSP2405105 & Rs 6,90,00,000 +GST
DELIVERY DATE	26 TH JAN 2027 (24 months)
1 ST STAGE OF PAYMENT-	10% ON APPROVAL OF QAP,PERT,MPP,MSTP HT & UT,NDE PLAN & PROCEDURE- PAYMENT RECEIVED
2 ND STAGE OF PAYMENT-	15% ON PROCUREMENT OF MAJOR RAW MATERIAL – WAITING FOR BARC APPROVAL.
3 RD & 4 TH STAGE OF PAYMENT	----

TEAM MEMBERS


- **ANIL KUMAR, SCT-D - PROJECT CO-ORDINATOR**
- **CHAMPURI SRINIVAS RAO, SCT-D – QUALITY & INSPECTION**
- **BHARAT P, SCT-D – MANUFACTURING**
- **SANDEEP KR, TECHNICAL ASSISTANT - ASSEMBLY & TESTING**
- **SK VERMA - TECHNICAL CONSULTANT**
- **MUKKANNESHWARA KN, PROJECT ASSOCIATE - DESIGN**




PROJECT -1: MFG & SUPPLY OF SPECIAL TOOLINGS & EQUIPMENTS

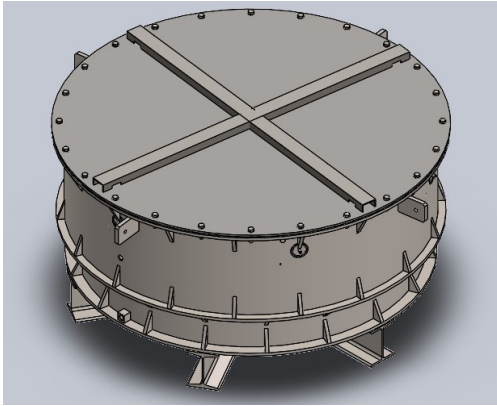


CONTAINER

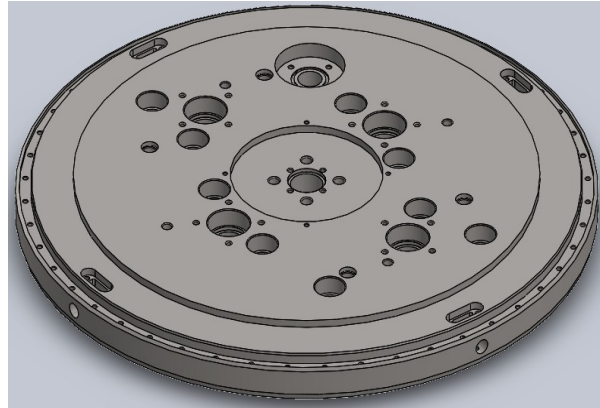


FLUSHING PLATE

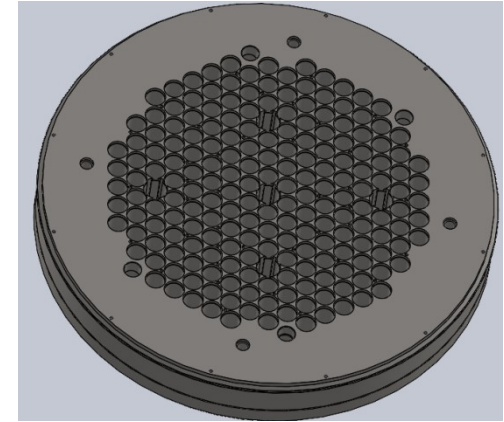


LOADING PLATE

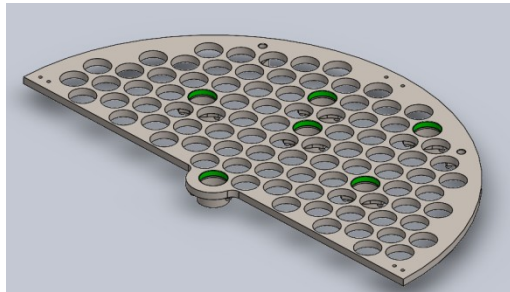

IGP,TGP &BGP

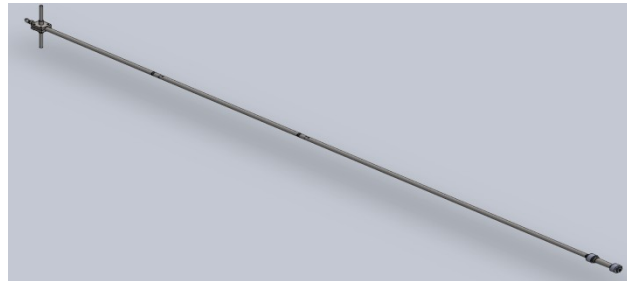

REAMER & GAUGES ASSY

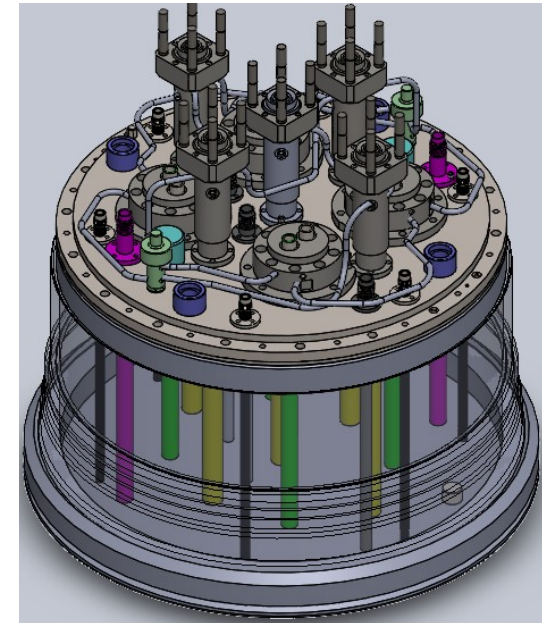

COVER SIMULATOR



PROJECT – 1: MFG & SUPPLY OF SPECIAL TOOLINGS & EQUIPMENTS

STATUS OF DOCUMENTATION:

SL. NO.	DESCRIPTION	QTY	STATUS
1	DESIGN, 3D MODELLING OF THE COMPONENTS & ASSEMBLY	166	SUBMITTED AND APPROVED BY BARC
2	FEM ANALYSIS OF CONTAINERS	3	SUBMITTED AND APPROVED BY BARC
2	DRAWINGS	166	166 PART DRAWINGS APPROVED 15 GA DRAWINGS APPROVED.
3.	QAP & MSTPS	13	APPROVED BY BARC.
4	WELDING ,NDE,INSPECTION & TESTING,HEAT TREATMENT	4	APPROVED BY BARC
5	TECHNOLOGICAL PROCESS SHEETS	23	APPROVED BY BARC



PROJECT – 1: MFG & SUPPLY OF SPECIAL TOOLINGS & EQUIPMENTS

STATUS OF RAW MATERIAL:

SL. NO.	DESCRIPTION	QTY	STATUS
1	RODS,BARS & PLATES (SS304/304L/420/17-4PH)	35	ALL ITEMS RECEIVED
2	SA 312 PIPES	15	UNDER PROGRESS EDC-25/07/2026
3	AISI 1020 BARS	6	UNDER PROGRESS EDC-20/07/2026



PROJECT – 1: MFG & SUPPLY OF SPECIAL TOOLINGS & EQUIPMENTS

STATUS OF MANUFACTURING :

Sl. No	DESCRIPTION	QTY	STATUS
1	IN HOUSE COMPONENTS (PLUGS,NOZZLES,GAUGES, SHAFT, GUIDESLEEVES, CONICAL SLEEVES, EXTENDERS BGP, TGP & IGP)	550	90% OF THE IN-HOUSE COMPONENTS HAVE COMPLETED ROUGH MACHINING. EDC-26/07/2026
2	OUT-SOURCE COMPONENTS (CONTAINERS, FLUSHING PLATE,LOADING PLATE,COVER SIMULATOR)	50	- TWO PLUG CONTAINERS ARE 70% COMPLETED & MATERIAL CUTTING FOR THE REMAINING WORK IS IN PROGRESS. EDC-26/07/2026



PROJECT – 1: MFG & SUPPLY OF SPECIAL TOOLINGS & EQUIPMENTS

STATUS OF BOUGHTOUT ITEMS:

SL . NO	DESCRIPTION	QTY.	STATUS
1	BOUGHTOUT ITEMS(PARKER FITTINGS,DAIL GAUGES, PRESSURE GAUGGES,BOLTS, NUTS,EYE BOLTS Etc.)	60	UNDER PROGRESS EDC-15/07/2026



PERT CHART



RAW MATERIAL STATUS

- **SS 304L FORGINGS FROM CHW FORGE (GHAZIABAD)**



RAW MATERIAL STATUS

- SS 304L & 420 PLATES AND BARS FROM REXINO, MUMBAI



RAW MATERIAL STATUS

- 17-4 PH SS FROM VICTOR STEEL, PEENYA BANGALORE




RAW MATERIAL STATUS

- SS 304 LASER CUT SECTORS OF LOADING PLATE



PERT CHART

MANUFACTURING & SUPPLY OF SPECIAL FASTENERS AND SEALS FOR B11-STEAM GENERATION PLANT (SGP)

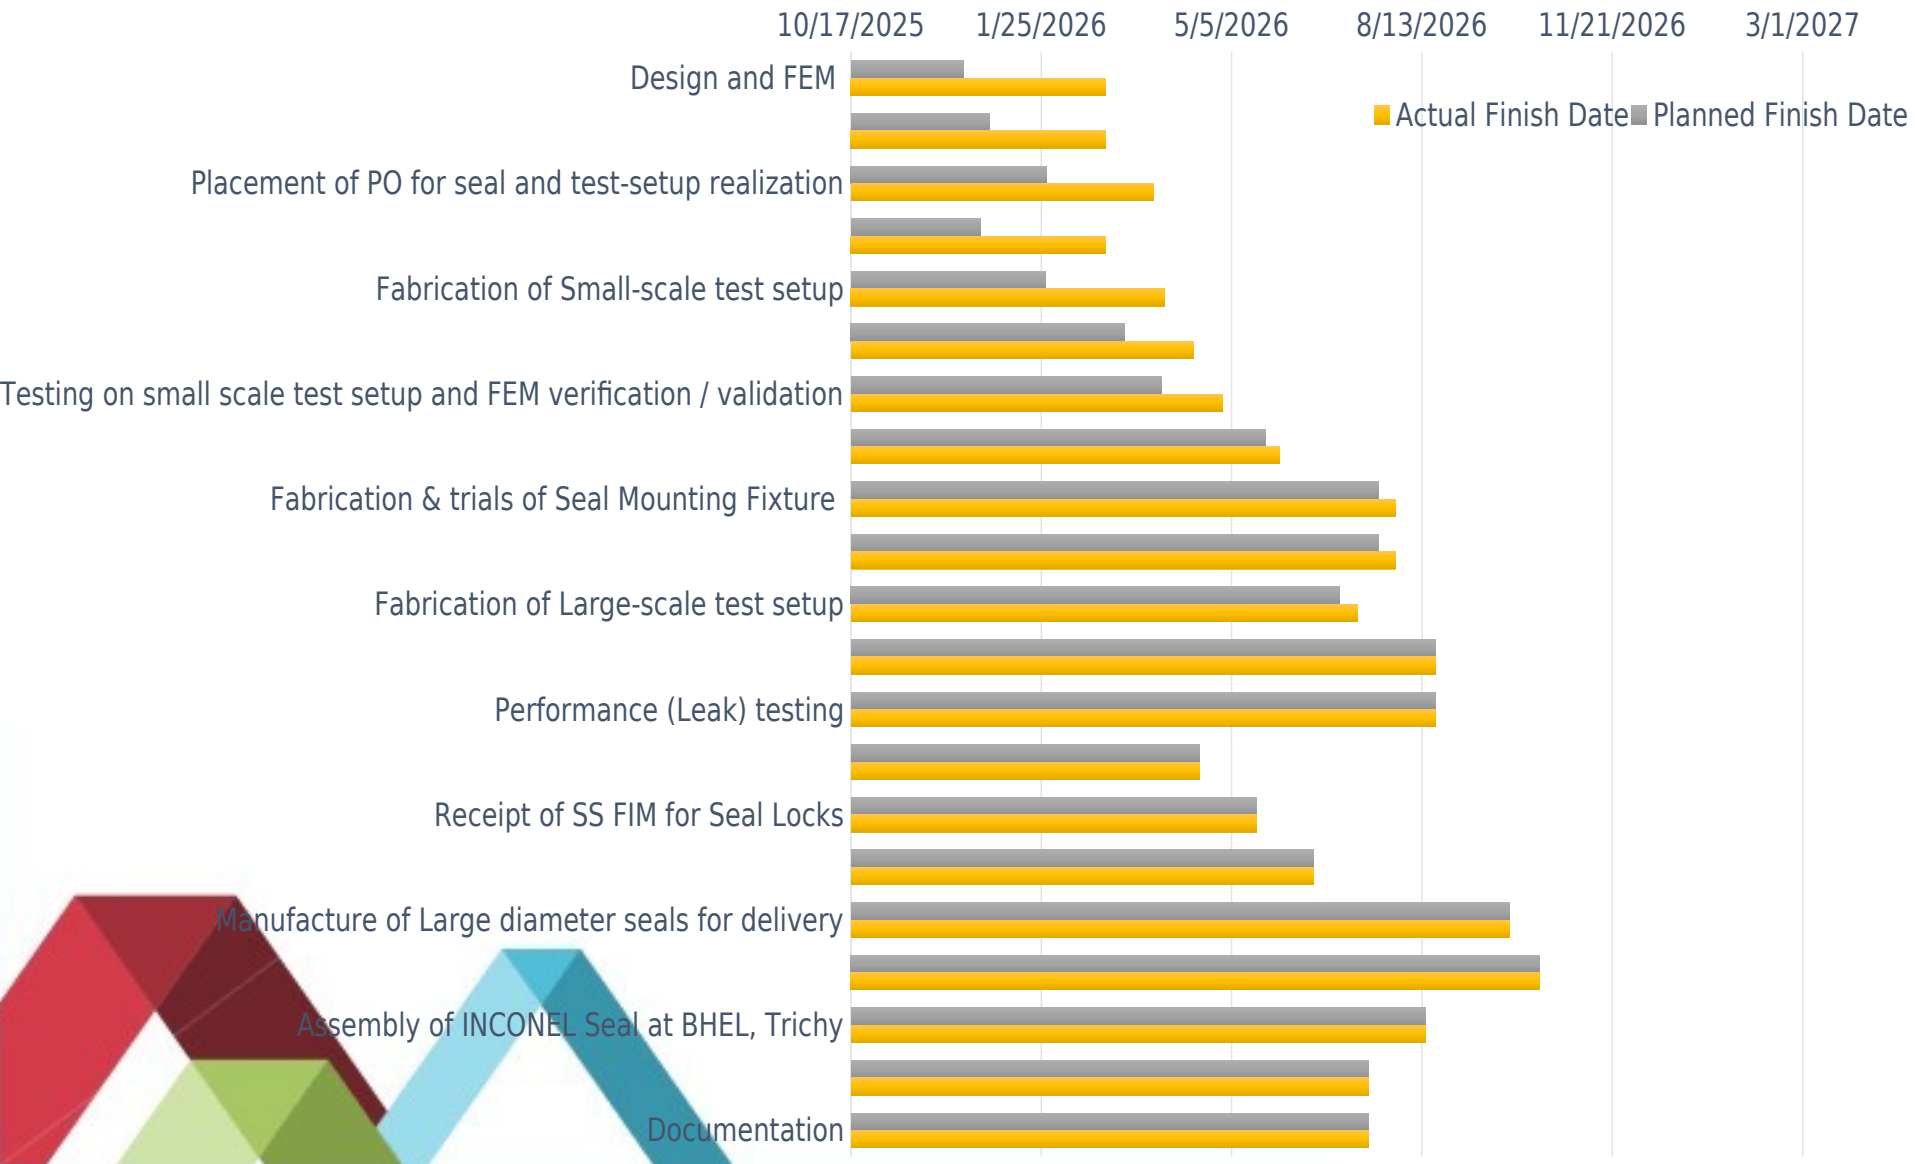



THANK YOU
