

PROJECT REVIEW MEETING

PROJECT	MANUFACTURING AND SUPPLY OF SPECIAL TOOLINGS AND EQUIPMENTS
ATVP PO NO	1/N/072/REF/EQPT, 27 TH JAN 2025
CMTI PROJECT NO AND VALUE	GSP2405105 & Rs 6,90,00,000 +GST
DELIVERY DATE	26 TH JAN 2027 (24 months)
1 ST STAGE OF PAYMENT-	10% ON APPROVAL OF QAP,PERT,MPP,MSTP HT & UT,NDE PLAN & PROCEDURE- INVOICE RAISED
2 ND STAGE OF PAYMENT-	15% ON PROCUREMENT OF MAJOR RAW MATERIAL –REQUEST PPM TO RAISE INVOICE FOR 2 ND STAGE
3 RD & 4 TH STAGE OF PAYMENT	----

PROJECT – 1: MFG & SUPPLY OF SPECIAL TOOLINGS & EQUIPMENTS

TEAM MEMBERS


- **ANIL KUMAR, SCT-D, PROJECT CO-ORDINATOR**
- **CHAMPURI SRINIVAS RAO, SCT-D , QUALITY & INSPECTION**
- **BHARAT P, SCT-D , MANUFACTURING**
- **SANDEEP KR, TECHNICAL ASSISTANT , ASSEMBLY & TESTING**
- **SK VERMA, TECHNICAL CONSULTANT**
- **MUKKANNESHWARA KN, PROJECT ASSOCIATE , DESIGN**




PROJECT – 1:MFG & SUPPLY OF SPECIAL TOOLINGS & EQUIPMENTS




www.cmti-india.net

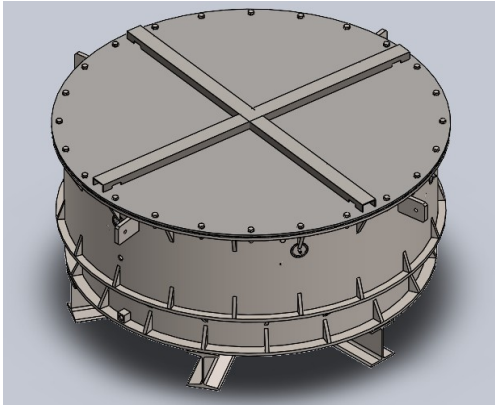


CONTAINER

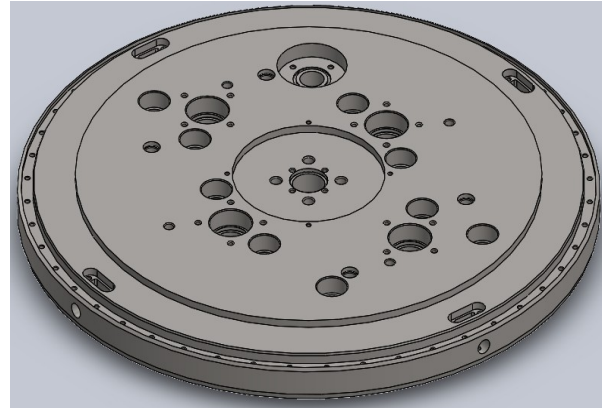


FLUSHING PLATE

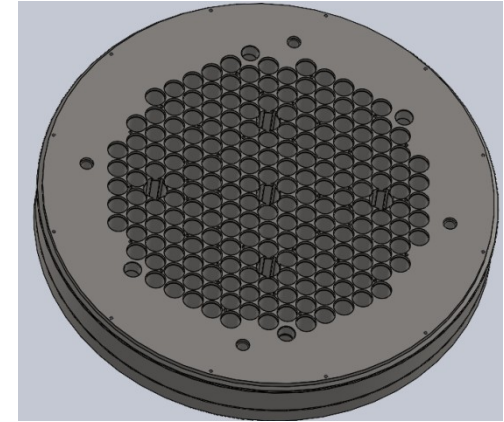


LOADING PLATE

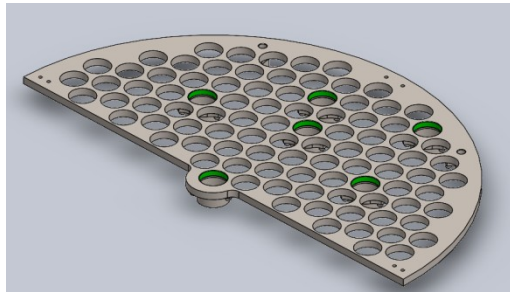

IGP,TGP &BGP

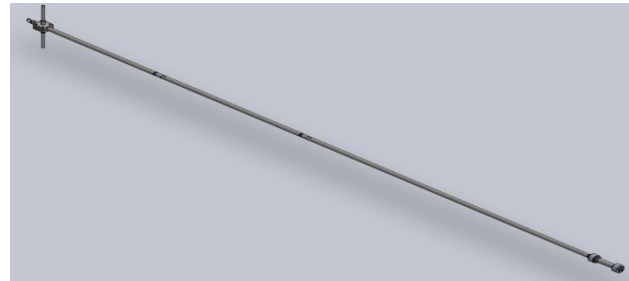

REAMER & GAUGES ASSY

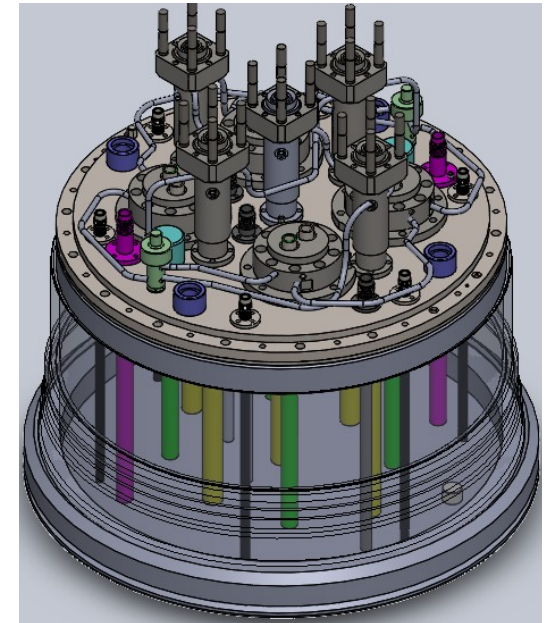

COVER SIMULATOR



PROJECT – 1: MFG & SUPPLY OF SPECIAL TOOLINGS & EQUIPMENTS

STATUS OF DOCUMENTATION:

SL. NO.	DESCRIPTION	QTY	STATUS
1	DESIGN, 3D MODELLING OF THE COMPONENTS & ASSEMBLY	166	SUBMITTED AND APPROVED BY BARC
2	FEM ANALYSIS OF CONTAINERS	3	SUBMITTED AND APPROVED BY BARC
2	DRAWINGS	166	166 PART DRAWINGS APPROVED 15 GA DRAWINGS APPROVED.
3.	QAP & MSTPS	13	APPROVED BY BARC.
4	WELDING ,NDE,INSPECTION & TESTING,HEAT TREATMENT	4	APPROVED BY BARC
5	TECHNOLOGICAL PROCESS SHEETS	23	• 11 PREPARED & SUBMITTED TO BARC • 12 UNDER PREPARATION

PROJECT – 1: MFG & SUPPLY OF SPECIAL TOOLINGS & EQUIPMENTS

STATUS OF RAW MATERIAL:

SL. NO.	DESCRIPTION	QTY	STATUS
1	RODS,BARS & PLATES (SS304/304L/420/17-4PH)	35	ALL ITEMS RECEIVED AT CMTI AND BARC APPROVED
2	SA 312 PIPES	15	NOT YET STARTED EDC-25/04/2026
3	AISI 1020 BARS	6	NOT YET STARTED EDC-20/04/2026



PROJECT – 1: MFG & SUPPLY OF SPECIAL TOOLINGS & EQUIPMENTS

STATUS OF MANUFACTURING :

SI .N o	DESCRIPTION	QT Y	STATUS
1	IN HOUSE COMPONENTS (PLUGS,NOZZLES,GAUGES, SHAFT, GUIDESLEEVES, CONICAL SLEEVES, EXTENDERS BGP,TGP & IGP)	550	358 PLUGS ROUGH MACHINING IS COMPLETED AND 358 NOS SENT FOR HT. - OTHER ITEMS NOT YET STARTED EDC-26/07/2026
2	OUT-SOURCE COMPONENTS (CONTAINERS, FLUSHING PLATE,LOADING PLATE,COVER SIMULATOR)	50	COMMERCIAL NEGOTIATION IS COMPLETED & PO YET TO BE PLACED. EDC-26/07/2026



PROJECT – 1: MFG & SUPPLY OF SPECIAL TOOLINGS & EQUIPMENTS



www.cmti-india.net

STATUS OF BOUGHTOUT ITEMS:

SL . NO	DESCRIPTION	QTY .	STATUS
1	BOUGHTOUT ITEMS(PARKER FITTINGS,DAIL GAUGES, PRESSURE GAUGGES,BOLTS, NUTS,EYE BOLTS Etc..)	60	NOT YET STARTED EDC-15/04/2026

ASSEMBLY TESTING .

SL .N O	DESCRIPTION	QTY.	STATUS
1	ASSEMBLY AND TESTING	6	NOT YET STARTED

PERT CHART



RAW MATERIAL STATUS

- SS 304L FORGINGS FROM CHW FORGE (GHAZIABAD)



RAW MATERIAL STATUS

- SS 304L & 420 PLATES AND BARS FROM REXINO, MUMBAI



RAW MATERIAL STATUS

- 17-4 PH SS FROM VICTOR STEEL, PEENYA BANGALORE



RAW MATERIAL STATUS

- SS 304 LASER CUT SECTORS OF LOADING PLATE





THANK YOU
